

# Change Order

No. 2

Date of Issuance: <u>June 25, 2023</u> Effective Date: <u>June 25, 2023</u>	
Project: Mangana Hein Road Extension Project	
Contract: Construction Contract Mangana Hein Road Extension Project	Date of Contract: February 9, 2023
Owner: Webb County	Contractor: Anderson Columbia Co., Inc.

**The Contract Documents are modified as follows upon execution of this Change Order:**

Description:  
Existing road base material is not suitable for pavement due to it being too clayish and holding moisture:

QUANTITY	UM	Description	Unit price	Extended Amount
1.00	LS	Additional Work*	\$ 166,316.16	\$166,316.16
5,880.00.	SY	8" Flexible Base (Crushed Concrete)	\$ 18.26	\$107,368.80
1.00	LS	Reversing Crushed Concrete Credit ***	\$(26,320.00)	(\$26,320.00)

**Total** **\$300,004.96**

\*Includes Mobilization, Excavation Cut, Subgrade Preparation, Geogrid, and MC-30 (5,880sy).

\*\*\* Credited as per submittal #2.

**Attachments (list documents supporting change):**

Attachment A - Proposal Dated 10/12/2023.

CHANGE IN CONTRACT PRICE:	CHANGE IN CONTRACT TIMES:
Original Contract Price: <u>\$2,235,770.00</u>	Original Contract Times: <u>ONE HUNDRED TWENTY (120) CALENDAR DAYS</u>
	Completion (days or date): <u>ONE HUNDRED TWENTY (120) CALENDAR DAYS.</u>
Contract Price prior to this Change Order: <u>\$2,494,231.00</u>	Increase or Decrease in Calendar Days: <u>No increase or Decrease in Calendar days.</u>
	Completion (days): <u>ONE HUNDRED TWENTY (120) CALENDAR DAYS.</u>
Increase of this Change Order: <u>Up to \$300,004.96</u>	Contract Times prior to this Change Order: <u>ONE HUNDRED TWENTY (120) CALENDAR DAYS.</u>
	Completion (days or date): <u>ONE HUNDRED TWENTY (120) CALENDAR DAYS.</u>

FILED 11/8 2023 11:00 AM  
 MARGIE RAMIREZ IBARRA  
 COUNTY CLERK, WEBB COUNTY TEXAS  
 BY A. Reza DEPUTY

Mangana Hein Road Extension Project

Contract Price incorporating this Change Order: Up to <u>\$2,794,235.96</u>	Completion (days or date): ONE HUNDRED TWENTY (120) CALENDAR DAYS.
--	--

The parties agree that the foregoing Change Order shall be hereinafter considered a part of the contract referred to above and incorporated by reference therein for all purposes. The amendments shall be subject to any and all other provisions of the contract which are hereby ratified by the parties and remain in full force and effect, with the exception of the parts or provisions of the contract which have been modified by this Change Order.

ACCEPTED:

ACCEPTED:

Owner (Authorized Signature)

Contractor (Authorized Signature)


By:   
 Tano E. Tijerina  
 Webb County Judge

By:   
 Berry O'Bryan  
 Vice President

Date: June 25, 2023

Date: June 25, 2023

ATTEST:

  
 Margie Ramirez Ibarra  
 Webb County Clerk




# Proposal

Anderson Columbia Co., Inc.  
 8114 State Highway 359  
 Laredo, Texas 78043  
 (956)-726-9819

Date: 10/12/2023

TO:  
 Webb County  
 1110 Washington street  
 Laredo, TX 78040  
 (956)523-4055

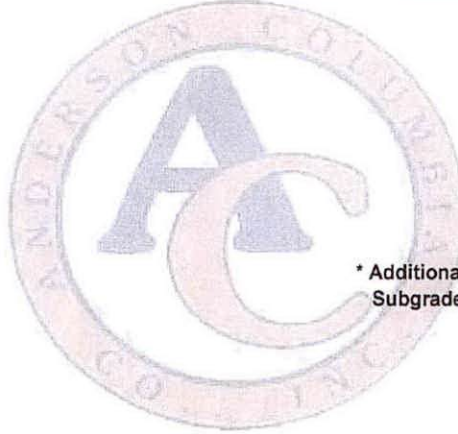

\* Additional work includes Mobilization, Excavation Cut, Subgrade Preparation, Geogrid, and MC-30 (5,880sy)

Project:  
 Mangana Hein Road Extension  
 Webb Co.  
 ITB: 2022-015

QUANTITY	UM	DESCRIPTION	Unit price	Extended Amount
1.00	LS	Additional Work *	\$ 166,316.16	\$166,316.16
5,880.00	SY	8" Flexible Base (Crushed Concrete), in place	\$ 18.26	\$107,368.80
1.00	LS	Reversing Crushed Concrete Credit	\$ 26,320.00	\$26,320.00
			Total	\$300,004.96
				<b>\$300,004.96</b>
