

PRESTIEGE

Innovators Construction Inc.

Contract Agreement Date: JUNE _____, 2016

BETWEEN the Owner:

THE COUNTY OF WEBB
1000 HOUSTON ST. 3RD FLOOR
LAREDO TX. 78040

and the **Contractor**:

PRESTIEGE INNOVATORS CONSTRUCTION INC.
DBA MODESTO ALONZO MARTINEZ
14402 EXPORT RD
LAREDO TX. 78045

for the following **Project**:

RFP-2016-02-1 LA PRESA SOCCER FIELD IMPROVEMENTS

The **Architect** is:

THE COUNTY OF WEBB ENGINEERING DEPARTMENT
1000 HOUSTON ST.
LAREDO TX. 78040

The Owner and Contractor agree as follows.

TABLE OF ARTICLES

1	THE CONTRACT DOCUMENTS
2	DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION DATE
3	CONTRACT SUM
4	PAYMENT
5	INSURANCE
6	GENERAL PROVISIONS
7	OWNER
8	CONTRACTOR
9	ARCHITECT
10	CHANGES IN THE WORK
11	TIME
12	PAYMENTS AND COMPLETION
13	PROTECTION OF PERSONS AND PROPERTY
14	CORRECTION OF WORK
15	MISCELLANEOUS PROVISIONS
16	TERMINATION OF THE CONTRACT
17	OTHER TERMS AND CONDITIONS

ARTICLE 1 THE CONTRACT DOCUMENTS

§ 1.1 The Contractor shall complete the Work described in the Contract Documents for the project. The Contract Documents consist of:

- .1 this Agreement signed by the Owner and Contractor;
- .2 the drawings and specifications prepared by the Architect, dated _____, and enumerated as follows:

Drawings:

Number	Title	Date
1	RFP 2016-02-1	04/25/2016

Specifications:

Section	Title	Pages
	RFP 2016-02-1	5

- .3 addenda prepared by the Architect as follows:

Number	Date	Pages
1	04/25/2016	

- .4 written change orders or orders for minor changes in the Work issued after execution of this Agreement; and
- .5 other documents, if any, identified as follows: Terms, conditions and specifications set forth in Webb county RFP 2016-02-1, a copy of which is attached hereto as Exhibit "1"

ARTICLE 2 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION

The number of calendar days available to the Contractor to substantially complete the Work is he Contract Time. The date of commencement of the work shall be the date of this Agreement unless otherwise indicated below. The Contractor shall substantially complete the Work not later than NINETY (90) calendar days from the date of commencement, subject to adjustment as provided in Article 10 and Article 11. *(Insert the date of commencement, if it differs from the date of this Agreement.)*

COMMENCEMENT DATE TO BE ISSUED BY THE COUNTY OF WEBB ENGINEERING DEPT.

ARTICLE 3 CONTRACT SUM

§3.1 Subject to additions and deductions in accordance with Article 10, the Contract Sum is:

ONE HUNDRED FORTY TWO THOUSAND DOLLARS AND ZERO CENTS (\$ 142,000.00)



§3.2 For purposes of payment, the Contract Sum includes the following values related to portions of the Work: *(itemize the Contract Sum among the major portions of the Work.)*

Portion of Work	Value
LUMP SUM	142,000.00

§3.3 Unit prices, if any, are as follows: *(Identify and state the unit price; state the quantity limitations, if any, to which the unit price will be applicable.)*

Item	Units and Limitations	Price per Unit (\$0.00)
N/A		

§3.4 Allowances included in the Contract Sum, if any, are as follows: *(Identify allowance and state exclusions, if any, from the allowance price.)*

Item	Price (\$0.00)
N/A	

§3.5 The Contract Sum is based upon the following alternates, if any, which are described in the Contract Documents and hereby accepted by the Owner: *(State the numbers or other identification of accepted alternates. If the bidding proposal documents permit the Owner to accept other alternates subsequent to the execution of this Agreement, attach a schedule of such other alternates showing the amount for each and the date when that amount expires.)*

N/A

§3.6 The Contract Sum shall include all items and services necessary for the proper execution and completion of the Work.

ARTICLE 4 PAYMENT

§4.1 Based on Contractor's Applications for Payment certified by the Architect, the Owner shall pay the Contractor, in accordance with Article 12, as follows: *(Insert below timing for payments and provisions for withholding retainage, if any.)*

IN FOUR EQUAL PROGRESS PAYMENTS AFTER APPROVAL FROM WEBB COUNTY ENGINEERING & FINANCE DEPARTMENTS WITH A RETAINAGE OF 15% ON EACH OF THE FOUR (4) PROGRESS PAYMENTS, AS FOLLOWS.

- 1.) Progress Payment no. 1 upon 25% completion (less 15% retainage)
- 2.) Progress Payment no. 2 upon 50% completion (less 15% retainage)
- 3.) Progress Payment no. 3 upon 75% completion (less 15% retainage)
- 4.) Progress Payment no. 4 upon 100% completion (less 15% retainage)

ARTICLE 5 INSURANCE

§5.1 The Contractor shall provide Contractor's general liability and other Insurance as follows: *(Insert specific insurance requirements and limits.) Insurance shall be A rated or better in accordance with the Key Best Insurance Rating Guide*

Type of Insurance	Limit of Liability (\$0.00)
GENERAL LIABILITY	\$ 2,000,000.00
COMMERCIAL VEHICLE	
WORKERS COMP.	

§5.2 The Owner shall provide property insurance to cover the value of the Owner's property, including any Work provided under this Agreement. The Contractor is entitled to receive an increase in the Contract Sum equal to the insurance proceeds related to a loss for damage to the Work covered by the Owner's property insurance. Webb County shall be named as an additional insured party under the insurance policy.

§5.3 The Contractor shall obtain an endorsement to its general liability insurance policy to cover the Contractor's obligations under Section 8.12.

§5.4 Each party shall provide certificates of insurance showing their respective coverages prior to commencement of the Work.

§5.5 Unless specifically precluded by the Owner's property insurance policy, the Owner and Contractor waive all rights against (1) each other and any of their subcontractor's suppliers, agents and employees, each of the other; and (2) the Architect, Architect's consultants and any of their agents and employees, for damages caused by fire or other causes of loss to the extent covered by property insurance or other insurance applicable to the Work.

ARTICLE 6 GENERAL PROVISIONS

§6.1 THE CONTRACT

The Contract represents the entire and integrated agreement between the parties and supersedes prior negotiations, representations or agreements, either written or oral. The Contract may be amended or modified only by a written modification in accordance with Article 10.

§6.2 THE WORK

The term "Work" means the construction and services required by the Contract Documents, and includes all other labor materials, equipment and services provided, or to be provided, by the Contractor to fulfill the Contractor's obligations.

§6.3 INTENT

The intent of the Contract Documents is to include all items necessary for the proper execution and completion of the Work by the Contractor. The Contract Documents are complementary, and what is required by one shall be as binding as if required by all.

§6.4 OWNERSHIP AND USE OF ARCHITECT'S DRAWINGS, SPECIFICATIONS AND OTHER DOCUMENTS

Documents prepared by the Architect are instruments of the Architect's service for use solely with respect to this Project. The Architect shall retain all common law, statutory and other reserved rights, including the copyright. The Contractor, subcontractors, sub-subcontractors, and material or equipment suppliers are authorized to use and reproduce the instruments of service solely and exclusively for execution of the Work. The instruments of service may not be used for other Projects or for additions to this Project outside the scope of the Work without the specific written consent of the Architect.



ARTICLE 7 OWNER

§7.1 INFORMATION AND SERVICES REQUIRED OF THE OWNER

§7.1.1 If requested by the Contractor, the Owner shall furnish all necessary surveys and legal description of the site.

§7.1.2 Except for permits and fees that are the responsibility of the Contractor under the Contract Documents, the Owner shall obtain and pay for other necessary approvals, easements, assessments and charges.

§7.2 OWNER'S RIGHT TO STOP THE WORK

If the Contractor fails to correct Work which is not in accordance with the Contract Documents, the Owner may direct the Contractor in writing to stop the Work until the correction is made.

§7.3 OWNER'S RIGHT TO CARRY OUT THE WORK

If the Contractor defaults or neglects to carry out the Work in accordance with the Contract Documents and fails within a seven day period after receipt of written notice from the Owner to commence and continue correction of such default or neglect with diligence and promptness, the Owner may, without prejudice to other remedies, correct such deficiencies. In such case, the Contract Sum shall be adjusted to deduct the cost of correction from payments due the Contractor.

§7.4 OWNER'S RIGHT TO PERFORM CONSTRUCTION AND TO AWARD SEPARATE CONTRACTS

§7.4.1 The Owner reserves the right to perform construction or operations related to the Project with the Owner's own forces, and to award separate contracts in connection with other portions of the Project.

§7.4.2 The Contractor shall coordinate and cooperate with the Owner's own forces and separate contractors employed by the Owner.

§7.4.3 Costs caused by delays or by improperly timed activities or defective construction shall be borne by the party responsible therefor.

ARTICLE 8 CONTRACTOR

§8.1 REVIEW OF CONTRACT DOCUMENTS AND FIELD CONDITIONS BY CONTRACTOR

§8.1.1 Execution of the Contract by the Contractor is a representation that the Contractor has visited the site, become familiar with local conditions under which the Work is to be performed and correlated personal observations with requirements of the Contract Documents.

§8.1.2 The Contractor shall carefully study and compare the Contract Documents with each other and with information furnished by the Owner. Before commencing activities, the Contractor shall (1) take field measurements and verify field conditions with Architect in writing (2) carefully compare this and other information known to the Contractor with the Contract Documents; and (3) promptly report errors, inconsistencies or omissions discovered to the Architect in writing.

§8.2 CONTRACTOR'S CONSTRUCTION SCHEDULE

The Contractor, promptly after being awarded the Contract, shall prepare and submit for the Owner's and Architect's information a Contractor's construction schedule for the Work.

§8.3 SUPERVISION AND CONSTRUCTION PROCEDURES

§8.3.1 The Contractor shall supervise and direct the Work, using the Contractor's best skill and attention. The Contractor shall be solely responsible for and have control over construction means, methods, techniques, sequences and procedures, and for coordinating all portions of the Work.

§8.3.2 The Contractor, as soon as practicable after award of the Contract, shall furnish in writing to the Owner through the Architect the names of subcontractors or suppliers for each portion of the Work. The Contractor shall not contract with any subcontractor or supplier to whom the Owner or Architect have made a timely and reasonable objection.

§8.4 LABOR AND MATERIALS

§8.4.1 Unless otherwise provided in the Contract Documents, the Contractor shall provide and pay for labor, materials, equipment, tools, utilities, transportation, and other facilities and services necessary for proper execution and completion of the Work.

§8.4.2 The Contractor shall enforce strict discipline and good order among the Contractor's employees and other persons carrying out the Contract Work. The Contractor shall not permit employment of unfit persons or persons not skilled in tasks assigned to them.

§8.5 WARRANTY

The Contractor warrants to the Owner and Architect that: (1) materials and equipment furnished under the Contract will be new and of good quality unless otherwise required or permitted by the Contract Documents; (2) the Work will be free from defects not inherent in the quality required or permitted; and (3) the Work will conform to the requirements of the Contract Documents, for a period of one year (1yr.) commencing from date of substantial completion as certified by the Architect.

§8.6 TAXES

The Contractor shall pay sales, consumer, use and similar taxes that are legally required when the Contract is executed.

§8.7 PERMITS, FEES AND NOTICES

§8.7.1 The Contractor shall obtain and pay for the building permit and other permits and governmental fees, licenses and inspections necessary for proper execution and completion of the Work.

§8.7.2 The Contractor shall comply with and give notices required by agencies having jurisdiction over the Work. If the Contractor performs Work knowing it to be contrary to applicable laws, statutes, ordinances, codes, rules, and regulations, or lawful orders of public authorities, the Contractor shall assume full responsibility for such Work and shall bear the attributable costs. The Contractor shall promptly notify the Architect in writing of any known inconsistencies in the Contract Documents with such governmental laws, rules and regulations.

§8.8 SUBMITTALS

The Contractor shall promptly review, approve in writing and submit to the Architect Shop Drawings, Product Data, Samples and similar submittals required by the Contract Documents. Shop Drawings, Product Data, Samples and similar submittals are not Contract Documents.

§8.9 USE OF SITE

The Contractor shall confine operations at the site to areas permitted by law, ordinances, permits, the Contract Documents and the Owner.

§8.10 CUTTING AND PATCHING

The Contractor shall be responsible for cutting, fitting or patching required to complete the Work or to make its parts fit together properly.

§8.11 CLEANING UP

The Contractor shall keep the premises and surrounding area free from accumulation of debris and trash related to the Work. At the completion of the Work, the Contractor shall remove its tools, construction equipment, machinery and surplus material; and shall properly dispose of waste materials.

§8.12 INDEMNIFICATION

To the fullest extent permitted by law, the Contractor shall indemnify and hold harmless the Owner, Architect, Architect's consultants and agents and employees of any of them from and against claims, damages, losses and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance of the Work, provided that such claims, damage, loss or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself), but only to the extent caused by the negligent acts or omissions of the Contractor, a subcontractor, anyone directly or indirectly employed by them or anyone for whose acts they may be liable, regardless of whether or not such claim, damage, loss or expense is caused in part by a party indemnified hereunder.

ARTICLE 9 ARCHITECT

§9.1 The Architect will provide administration of the Contract as described in the Contract Documents. The Architect will have authority to act on behalf of the Owner only to the extent provided in the Contract Documents.

§9.2 The Architect will visit the site at intervals appropriate to the stage of construction to become generally familiar with the progress and quality of the Work.

§9.3 The Architect will not have control over or charge of, and will not be responsible for, construction means, methods, techniques, sequences or procedures, or for safety precautions and program in connection with the Work, since these are solely the Contractor's responsibility. The Architect will not be responsible for the Contractor's failure to carry out the Work in accordance with the Contract Documents.

§9.4 Based on the Architect's observations and evaluations of the Contractor's Applications for Payment, the Architect will review and certify the amounts due the Contractor.

§9.5 The Architect has authority to reject Work that does not conform to the Contract Documents

§9.6 The Architect will promptly review and approve or take appropriate action upon the Contractor's submittals, but only for the limited purpose of checking conformance with information given and the design concept expressed in the Contract Documents.

§9.7 The Architect will promptly interpret and decide matters concerning performance under, and requirement of, the Contract Documents on written request from either the Owner or Contractor.

§9.8 Interpretations and decisions of the Architect will be consistent with the intent of and reasonably inferable from the Contract Documents and will be in writing or in the form of drawings. When making such interpretations and decisions, the Architect will endeavor to secure faithful performance by both Owner and Contractor, will not show partiality to either and will not be liable for results of interpretations or decisions rendered in good faith.

§9.9 The Architect's duties, responsibilities and limits of authority as described in the Contract Documents shall not be changed without written consent of the Owner, Contractor and Architect. Consent shall not be unreasonably withheld.

ARTICLE 10 CHANGES IN THE WORK

§10.1 The Owner, without invalidating the Contract, may order changes in the Work within the general scope of the Contract consisting of additions, deletions or other revisions, the Contract Sum and Contract Time being adjusted accordingly in writing. If the Owner and Contractor can not agree to a change in the Contract Sum, the Owner shall pay the Contractor actual cost plus reasonable overhead and profit.

§10.2 The Architect will have authority to order minor changes in the Work not involving changes in the Contract Sum or the Contract Time and not inconsistent with the intent of the Contract Documents. Such orders shall be in writing and shall be binding on the Owner and Contractor. The Contractor shall carry out such orders promptly.

§10.3 If concealed or unknown physical conditions are encountered at the site that differ materially from those indicated in the Contract Documents or from those conditions ordinarily found to exist, the Contract Sum and Contract Time shall be subject to equitable adjustment, which shall be in writing and signed and approved by Owner, Architect and Contractor prior to any such proposed equitable adjustment required.

ARTICLE 11 TIME

§11.1 Time limits stated in the Contract Documents are of the essence of the Contract.

§11.2 If the Contractor is delayed at any time in progress of the Work by changes ordered in the Work, or by labor disputes, fire, unusual delay in deliveries, unavoidable casualties or other causes beyond the Contractor's control, the Contract Time shall be subject to equitable adjustment.

ARTICLE 12 PAYMENTS AND COMPLETION**§12.1 CONTRACT SUM**

The Contract Sum stated in the Agreement, including authorized adjustments, is the total amount payable by the Owner to the Contractor for performance of the Work under the Contract Documents.

§12.2 APPLICATIONS FOR PAYMENT

§12.2.1 At least ten days before the date established for each progress payment, the Contractor shall submit to the Architect an itemized Application for Payment for Work completed in accordance with the values stated in the Agreement. Such Application shall be supported by data substantiating the Contractor's right to payment as the Owner or Architect may reasonably require. Payments shall be made on account of materials and equipment delivered and suitably stored at the site for subsequent incorporation in the Work. If approved in advance by the Owner, payment may similarly be made for materials and equipment stored, and protected from damage, off the site at a location agreed upon in writing.

§12.2.2 The Contractor warrants that title to all Work covered by an Application for Payment will pass to the Owner no later than the time of payment. The Contractor further warrants that upon submittal of an Application for Payment, all Work for which Certifies for Payment have been previously issued and payments received from the Owner shall, to the best of the Contractor's knowledge, information and belief, be free and clear of liens, claims, security interests or other encumbrances adverse to the Owner's interests.

§12.3 CERTIFICATES FOR PAYMENT

The Architect will, within seven days after receipt of the Contractor's Application for Payment, either issue to the Owner a Certificate for Payment, with a copy to the Contractor, for such amount as the Architect determines is properly due, or notify the Contractor and Owner in writing of the Architect's reasons for withholding certification in whole or in part.

§12.4 PROGRESS PAYMENTS

§12.4.1 After the Architect has issued a Certificate for Payment, the Owner shall make payment in the manner provided in the Contract Documents.

§12.4.2 The Contractor shall promptly pay each subcontractor and supplier, upon receipt of payment from the Owner, an amount determined in accordance with the terms of the applicable subcontracts and purchase orders.

§12.4.3 Neither the Owner nor the Architect shall have responsibility for payments to a subcontractor or supplier.

§12.4.4 A Certificate for Payment, a progress payment, or partial or entire use or occupancy of the Project by the Owner shall constitute acceptance of Work not in accordance with the requirements of the Contract Documents.

§12.5 SUBSTANTIAL COMPLETION

§12.5.1 Substantial Completion is the stage in the progress of the Work when the Work or designated portion thereof is sufficiently complete in accordance with the Contract Documents so the Owner can occupy or utilize the Work for its intended use, as determined and approved in writing and dated by the Architect to contractor as set forth herein-below.

§12.5.2 When the Work or designated portion thereof is substantially complete, the Architect will make an inspection to determine whether the Work is substantially complete. When the Architect determines that the Work is substantially complete the Architect shall prepare a Certificate of Substantial Completion that shall establish the date of Substantial Completion, shall establish responsibilities of the Owner and Contractor, and shall fix the time within which the Contractor shall finish all items on the list accompanying the Certificate. Warranties required by the Contract Documents shall commence on the date of Substantial Completion of the Work or designated portion thereof unless otherwise provided in the Certificate of Substantial Completion.

§12.6 FINAL COMPLETION AND FINAL PAYMENT

§12.6.1 Upon receipt of final Application for Payment, the Architect will inspect the Work. When the Architect finds the Work acceptable and the Contract fully performed, the Architect will promptly issue a final Certificate for Payment.

§12.6.2 Final payment shall not become due until the Contractor submits to the Architect releases and waivers of liens, and data establishing payment or satisfaction of obligations, such as receipts, claims, security interests or encumbrances arising out of the Contract.

§12.6.3 Acceptance of final payment by the Contractor, a subcontractor, or material supplier shall constitute a waiver of claims by that payee except those previously made in writing and identified by that payee as unsettled at the time of final Application for Payment.

ARTICLE 13 PROTECTION OF PERSONS AND PROPERTY

The Contractor shall be responsible for initiating, maintaining and supervising all safety precautions and programs, including all those required by law in connection with performance of the Contract. The Contractor shall make reasonable precautions to prevent damage, injury or loss to employees on the Work, the Work and materials and equipment to be incorporated therein, and other property at the site or adjacent thereto. The Contractor shall promptly remedy damage and loss to property caused in whole or in part by the Contractor, or by anyone for whose acts the Contractor may be liable.

ARTICLE 14 CORRECTION OF WORK

§14.1 The Contractor shall promptly correct Work rejected by the Architect as failing to conform to the requirements of the Contract Documents. The Contractor shall bear the cost of correcting such rejected Work, including the costs of uncovering, replacement and additional testing.

§14.2 In addition to the Contractor's other obligations including warranties under the Contract, the Contractor shall, for a period of one year after Substantial Completion, correct work not conforming to the requirements of the Contract Documents.

§14.3 If the Contractor fails to correct nonconforming Work within a reasonable time, the Owner may correct it in accordance with Section 7.3.

ARTICLE 15 MISCELLANEOUS PROVISIONS**§15.1 ASSIGNMENT OF CONTRACT**

Neither party to the Contract shall assign the Contract as a whole without written consent of the other.

§15.2 TESTS AND INSPECTIONS

§15.2.1 At the appropriate times, the Contractor shall arrange and bear cost of tests, inspections and approvals of portions of the Work required by the Contract Documents or by laws, statutes, ordinances, codes, ruled and regulations, or lawful orders of public authorities.

§15.2.2 If the Architect requires additional testing, the Contractor shall perform those tests.

§15.2.3 The Owner shall bear cost of test, inspections or approvals that do not become requirements until after the Contract is executed.

§15.3 GOVERNING LAW

The Contract shall be governed by the laws of the State of Texas where the Project is located. The exclusive venue for any litigation between the parties shall lie in Webb County, Texas.

ARTICLE 16 TERMINATION OF THE CONTRACT**§16.1 TERMINATION BY THE CONTRACTOR**

If the Architect fails to certify payment as provided in Section 12.3 for a period of 30 days through no fault of the Contractor, or if the Owner fails to make payment as provided in Section 12.4.1 for a period of 30 days, the Contractor may, upon seven additional days' written notice to the Owner and the Architect, terminate the Contract and recover from the Owner payment for Work executed including reasonable overhead and profit, and costs incurred by reason of such termination.

§16.2 TERMINATION BY THE OWNER FOR CAUSE

§16.2.1 The Owner may terminate the Contract if the Contractor

- .1 repeatedly refuses or fails to supply enough properly skilled workers or proper materials;
- .2 fails to make payment to subcontractors for materials or labor in accordance with the respective agreements between the Contractor and the subcontractors;
- .3 persistently disregards laws, ordinances, or rules, regulations or orders of a public authority having jurisdiction; or
- .4 is otherwise guilty of substantial breach of a provision of the Contract Documents.

§16.2.2 When any of the above reasons exist, the Owner, after consultation with the Architect, may without prejudice to any other rights or remedies of the Owner and after giving the Contractor and the Contractor's surety, if any, seven days' written notice, terminate employment of the Contractor and may

- .1 take possession of the site and of all materials thereon owned by the Contractor, and
- .2 finish the Work by whatever reasonable method the Owner may deem expedient.

§16.2.3 When the Owner terminates the Contract for one of the reasons stated in Section 16.2.1, the Contractor shall not be entitled to receive further payment until the Work is finished.

§16.2.4 If the unpaid balance of the Contract Sum exceeds costs of finishing the Work, such excess shall be paid to the Contractor. If such costs exceed the unpaid balance, the Contractor shall pay the difference to the Owner. This obligation for payment shall survive termination of the Contract.

§16.3 TERMINATION BY THE OWNER FOR CONVENIENCE

The Owner may, at any time, terminate the Contract for the Owner's convenience and without cause. The Contractor shall be entitled to receive payment for Work executed, and costs incurred by reason of such termination, along with a reasonable overhead and profit on the Work not executed.

ARTICLE 17 OTHER TERMS CONDITIONS

(Insert any other terms or conditions below.)

N/A

This Agreement entered into as of the day and year first written above.

(If required by law, insert cancellation period, disclosures or other warning statements above the signatures.)

N/A

OWNER (Signature)

CONTRACTOR (Signature)

(Printed name, title and address)

HON. TANO E. TIJERINA, COUNTY JUDGE

THE COUNTY OF WEBB TEXAS

1000 HOUSTON ST. 3RD FLOOR, LAREDO TX

(Printed name, title and address)

ALONZO MARTINEZ, PRESIDENT

PRESTIEGE INNOVATORS CONSTRUCCION

14402 EXPORT RD. LAREDO TX 78045

LICENSE NO. N/A

JURISDICTION N/A

ATTEST:

MARGIE RAMIREZ IBARRA
WEBB COUNTY CLERK

APPROVED AS TO FORM:

MARCO A. MONTEMAYOR
WEBB COUNTY ATTORNEY

*By law, the county attorney's Office may only advise or approve contracts or legal documents on behalf of its clients. It may not advise or approve a contract or legal document on behalf of other parties. Our review of this document was conducted solely from the legal perspective of our client. our approval of this document was offered solely for the benefit of our client. Other parties should not rely on this approval, and should seek review and approval of their own respective attorney(s).

Request for proposal (RFP) 2016-02-01/LA PRESA SOCCER FIELD/PRESTIEGE INNOVATORS CONSTRUCTION INC.

Approved by Webb County Commissioners Court on April 25, 2016 Item No. 17(i)



EXIBIT

" 1 "

Specifications for Artificial Turf

RFP - 2016-02

TECHNICAL DATA:

Type: ¾" tufted infilled synthetic grass carpet, straight stitch pattern

Pile content: 100% Ten Cate XP blade plus yarn, U.V. resistant, 10,000/1 denier, 100 microns

Primary backing: Double 100% PP Thiobac, black, U.V. - stabilized, weight ca. 7.82 oz/yd²

Secondary backing: Polyurethane coating, with drainage holes

Pile height	± 50mm +/- 10% ± 2 inch	+/- 10%		
Total thickness	± 52mm +/- 10% ± 2 inch	+/- 10%		
Stitch rate per 10 cm (width)	± 6,3			
Stitch rate per 10 cm (length)	± 17,5	+/- 1	± 13.34 per 3 inches	+/- 1
Number of tufts/m ²	± 11.025	+/- 5%	± 9,218/yd ²	+/- 5%
Face weight	± 1.355 gr/m ²	+/- 10%	± 40 oz/yd ²	+/- 10%
Weight primary backing	± 265 gr/m ²	+/- 10%	± 7.82 oz/yd ²	+/- 10%
Weight secondary backing	± 678 gr.m ²	+/- 10%	± 20 oz/yd ²	+/- 10%
Total weight	± 2.298 gr.m ²	+/- 10%	± 67.8 oz/yd ²	+/- 10%
Roll width	462 cm	+/- 2 cm	± 182 inch	+/- 0.8 inch
Roll length	as required			
Tuft bind	≥ 8 lbs			
Water permeability	± 13.2 gallon/yd ² /min (unfilled)			
Color fastness	Xenon test : blue-scale >7, grey-scale > 4			

COLOR:

Field green, White and Yellow for the line marking

INSTALLATION METHOD:

Loose laid on bound or unbound sub base, with or without a shock pad, glued or sewn seams

INFILL (RECOMMENDED):

All rubber or a mix of Silica Sand and SBR Rubber infill

PRODUCT APPLICATION:

Soccer, American Football, Baseball, Multifunctional


SPECIFICATIONS FOR SOCCER FIELD: (140 ft. x 80 ft.)

RFP - 2016-02

PERIMETER FOOTING:

1. 3000 psi, concrete
2. $\frac{3}{8}$ " U-joints
3. Wire mesh 6 x 6 x 6
4. $\frac{3}{8}$ " Rebar

Wall to be placed around the soccer field to hold synthetic turf at 140' x 80'
Dimension of wall itself to be buried 12" deep and be left at the ground level.
Wall is 12" deep and 6" wide. Will have 4 drain pipes, one @ each corner.
Other drain pipes will be placed every 30' alongside perimeter walls.

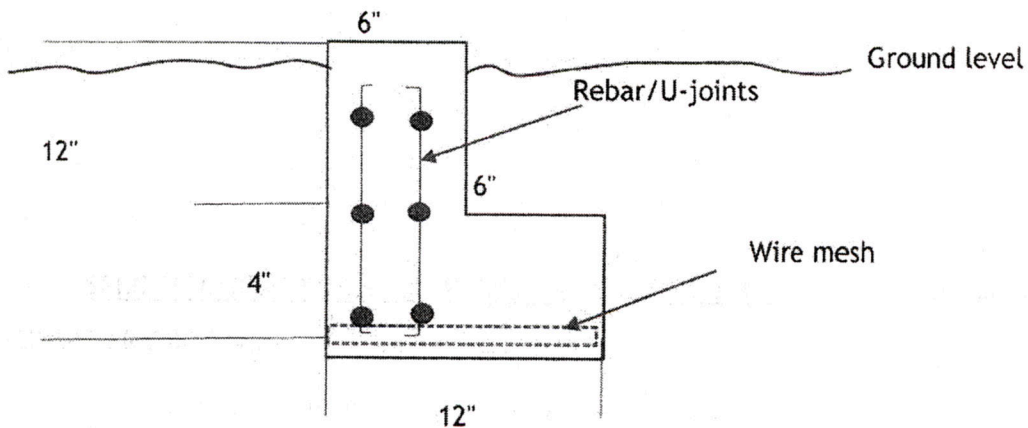

PLAYERS AREA:

One side to have concrete walk for players to function.

(2) 3000 psi concrete to be laid for 4' ft. x 4" inch deep all alongside of one 25' ft. sides and 2 player bench spaces of 8' by 15' Places on the same side of the concrete slab of the 2 aluminum 15' players bench to be installed.

SYNTHETIC TURF INSTALLATION:

Removal of dirt to 6.5" as specified, ground to be fumigated and a layer of geotextile fabric to be placed before the 4" compressed crushed limestone is installed. (Crushed limestone fine for pavers grade 3)

$\frac{1}{4}$ " padding to be laid after crushed limestone on all of the field. (Pad material is synthetic polymers padding $\frac{1}{4}$ " thick with black nylon support)

2" soccer grade turf to be installed with 1" of mix of crumb rubber turf and sand inlay. (Crumb rubber is industry standard for turf inlay)

Turf to be motorized brushed for the finish.

All dirt to be removed from premises after leveling all surrounding areas.

PRODUCT:

RFP - 2016-02

1. SlitFilm fiber material
2. Pile High 2" (+/- 1/8")
3. Pile Weight 40.oz per sq.yd.
4. Backing Weight 7.8 to 7.9 .oz sq.yd.
5. Total Weight 73.9 (+/-)
6. Tuff Bind 8lbs
7. 50/50 Mix of 3lbs sand per sq. ft. and 3lbs rubber per sq. ft. 1 - 1 1/2"
8. One field sweeper to be provided by contractor for maintenance of field 3' wide

OUTLINE AND FIELD MARKINGS:

Soccer field to be outlined with white turf & yellow turf to meet with specifications for play. Center stripe and circle, Goal area, Penalty area with 1/2 circle, 4 Corner areas and outside perimeter area.

EQUIPMENT:

Note the infield is 120 x 60 play area

NOTE TO BIDDERS:

Cost to be included for the cleaning and prep work for the proposed soccer field in the La Presa Community Center

**PRESTIEGE INNOVATORS
CONSTRUCTION INC.**

140 X 80 FIELD

RFP-2016-02-01
LA PRESA SOCCER FIELD

